

Agile Backlog Creation & Sprint Simulation in Jira

Digital Campus Library Reservation Gateway (DL2KS)

Name	Namith Kumar C
SRN	PES1UG24AM171
Section	C
Assignment	Lab 2 - Jira
Team member / Epic	Namith Kumar C - ISBN Catalog Management

Contents

1. Epic, User Stories and Story Points
2. Sprint Execution
3. Sprint Report and Burndown Chart
4. Reflection Questions


1. Epic, User Stories and Story Points

Epic **DL2KS-5 ISBN Catalog Management** has 6 user stories totalling **18 story points** (Fibonacci scale). Priority was set at story level based on user impact: the stories needed to build and search the catalog are High, supporting stories are Medium, and deleting a record is Low.

Key	User Story	Priority	Story Points
DL2KS-6	Add a Book to Catalog	High	3
DL2KS-7	Search Books by ISBN	High	3
DL2KS-8	View Book Details	Medium	2
DL2KS-9	Update Book Information	Medium	3
DL2KS-10	Delete a Book from Catalog	Low	2
DL2KS-11	Check Book Availability	High	5
Total	6 stories		18

Figure 1.1: Backlog - Stories with Priority, Story Points and Parent Epic

Backlog view before Sprint 2: DL2KS-9 (3 points, Medium), DL2KS-10 (2 points, Low) and DL2KS-11 (5 points, High), all in the ISBN Catalog Management epic with status To Do.

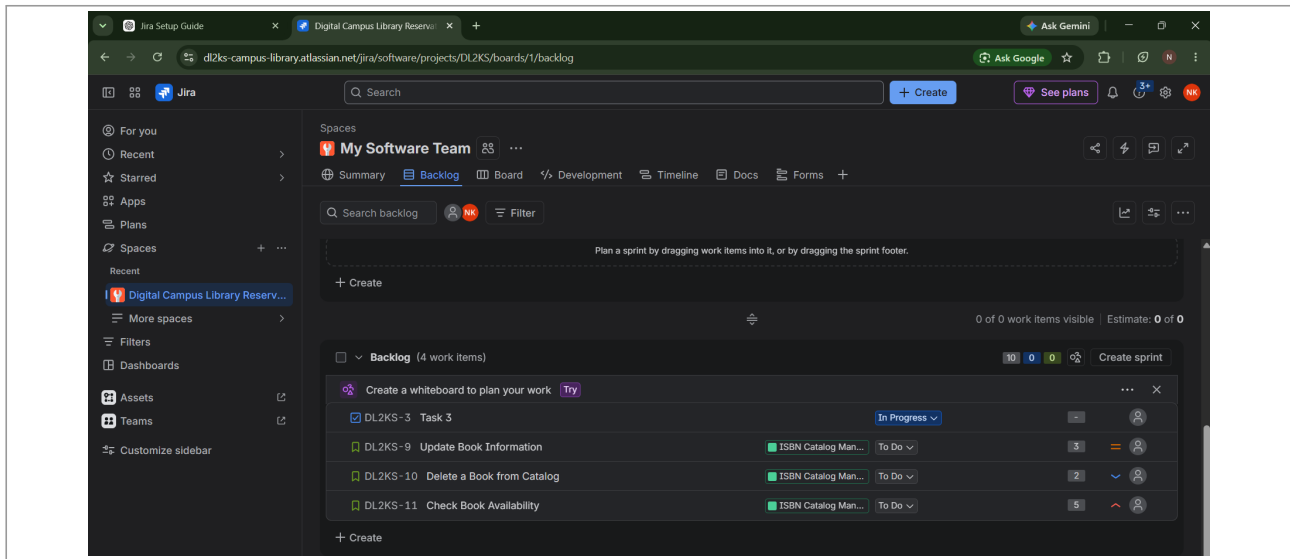

2. Sprint Execution

Sprint	Stories	Epic	Points	Sprint Goal	Result
Sprint 1 2 Oct - 9 Oct	DL2KS-6, DL2KS-7, DL2KS-8 (3 stories)	ISBN Catalog Management	8	Complete basic book catalog creation, ISBN search, and book detail viewing functionality.	3 of 3 Done
Sprint 2 3 Oct - 9 Oct	DL2KS-9, DL2KS-10, DL2KS-11 (3 stories)	ISBN Catalog Management	10	Complete book record maintenance, deletion, and availability checking functionality.	3 of 3 Done
Total	6 stories	1 epic	18		All Done

Sprint 1 (Figures 2.1 and 2.2)

Figure 2.1: Sprint 1 - Stories, Goal and Points

SCRUM Sprint 1 (2 Oct - 9 Oct, 3 work items) with its sprint goal. DL2KS-6 (3), DL2KS-7 (3) and DL2KS-8 (2) are Done; the sprint counter shows 8 points completed.


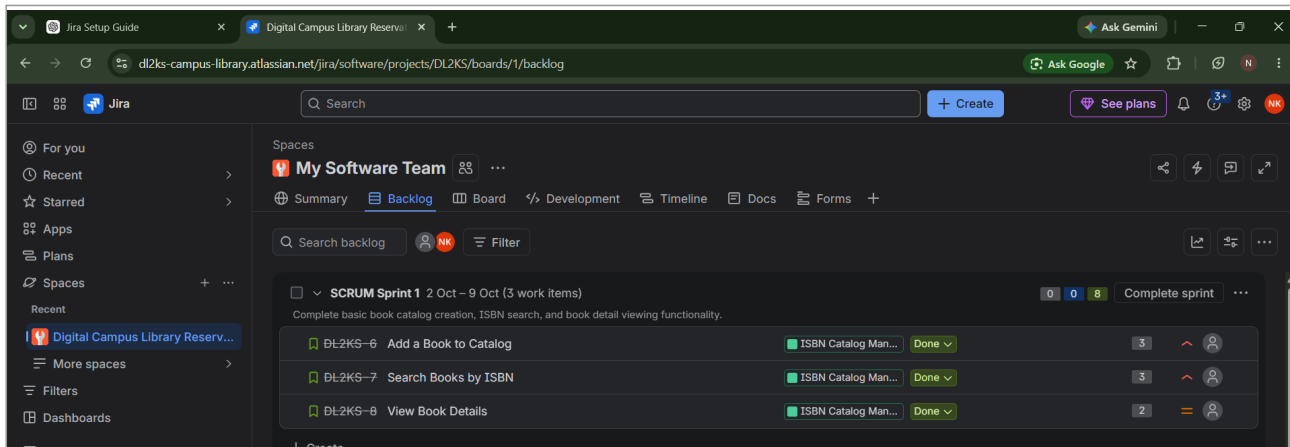


Figure 2.2: Sprint 1 Active Board (completed)

All three committed stories (Add a Book to Catalog, Search Books by ISBN, View Book Details) are in the Done column.

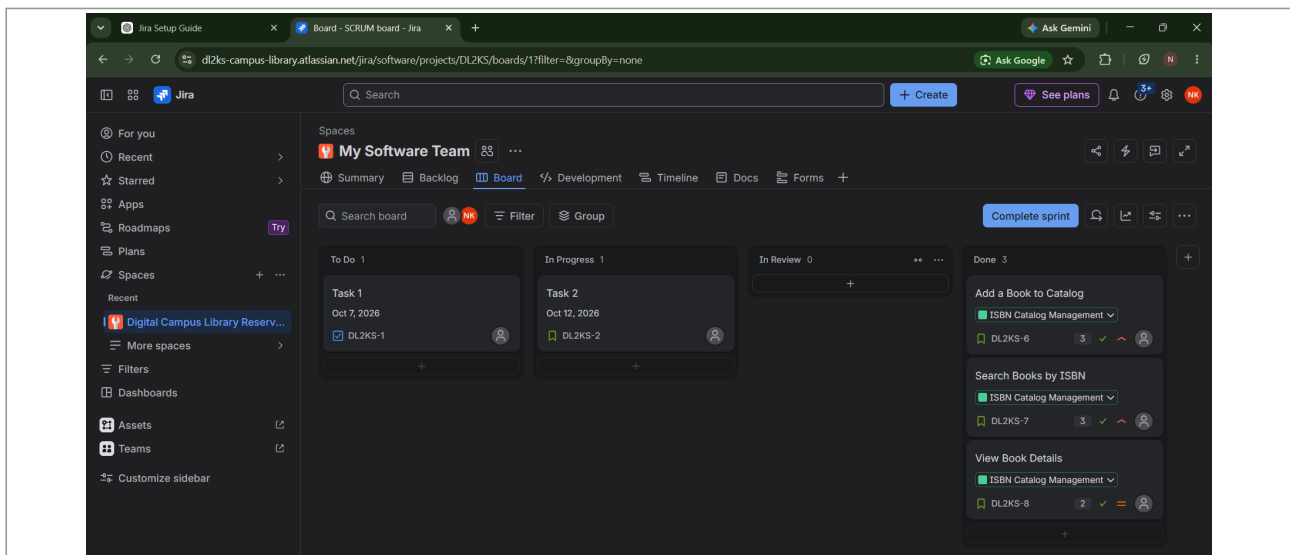

Sprint 2 (Figures 2.3 and 2.4)

Figure 2.3: Sprint 2 - Stories, Goal and Points

SCRUM Sprint 2 (3 Oct - 9 Oct, 3 work items) with its sprint goal. DL2KS-9 (3), DL2KS-10 (2) and DL2KS-11 (5) are Done; the sprint counter shows 10 points completed.


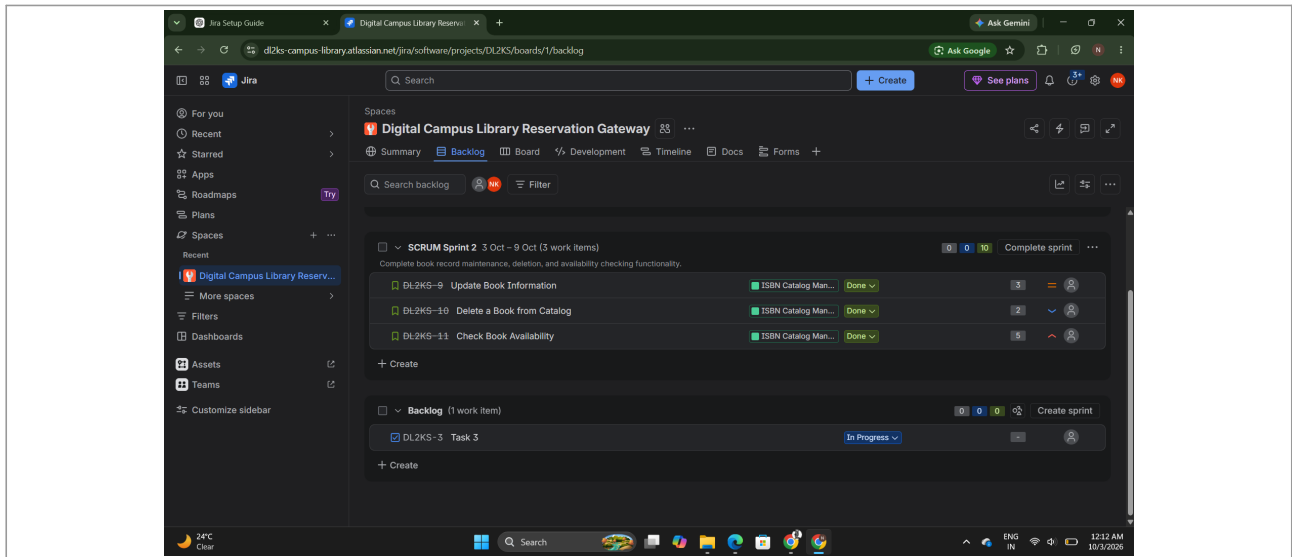


Figure 2.4: Sprint 2 Active Board (completed)

All three committed stories (Update Book Information, Delete a Book from Catalog, Check Book Availability) are in the Done column.

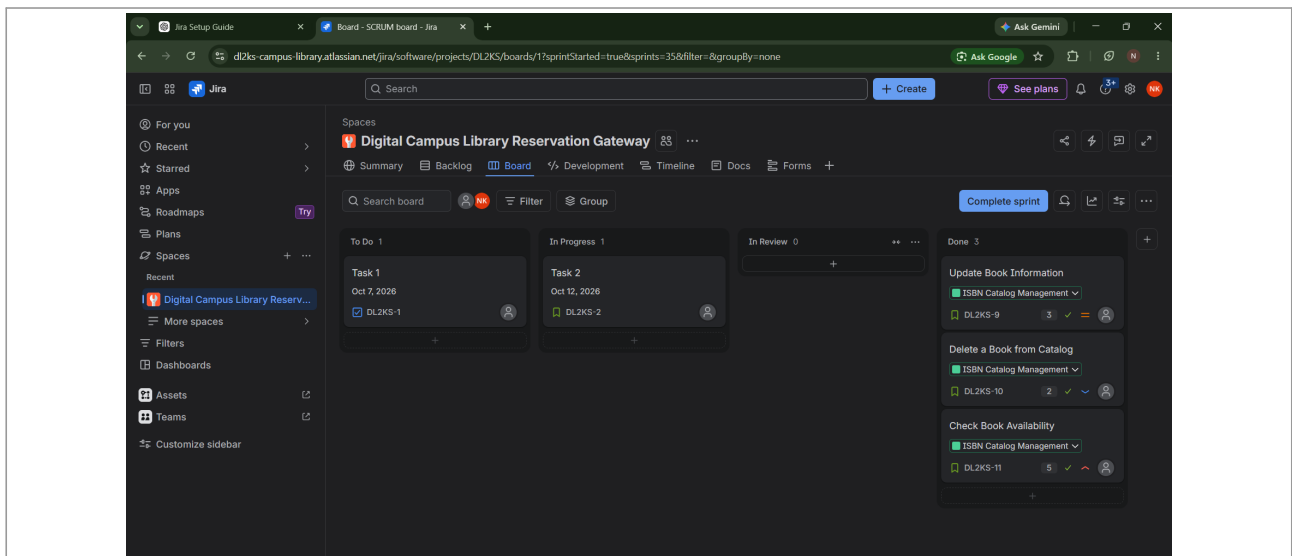

3. Sprint Report and Burndown Chart

Figure 3.1: Sprint 1 Insights - Sprint Progress, Burndown and Epic Progress

Sprint 1 shows 100% done, with 8 points done and 0 points to go. Remaining work falls from 100% to 0% well before the guideline reaches zero on 9 Oct. Epic progress for DL2KS-5 ISBN Catalog Management is shown as 100% done at the bottom of the panel.


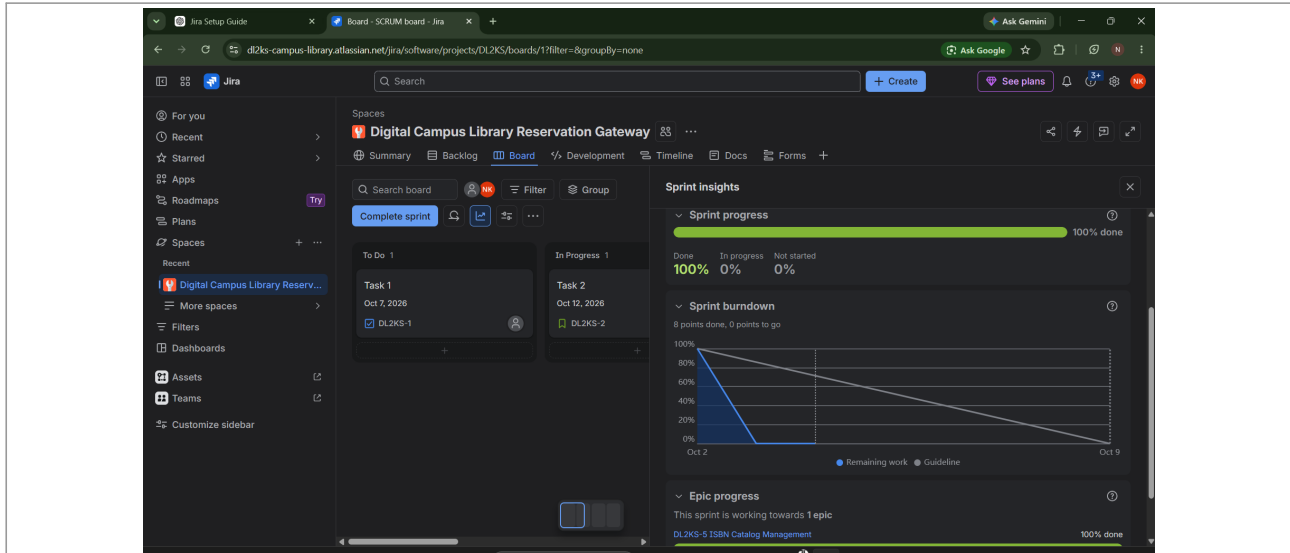


Figure 3.2: Sprint 2 Burndown Chart (story points)

Burndown for Sprint 2, generated from the sprint data: 10 points committed on 3 Oct and all 10 Done (3 of 3 stories) by 3 Oct, 12:12 AM, the time of the Sprint 2 backlog screenshot in Figure 2.3. The grey guideline shows the linear plan down to 0 on 9 Oct.

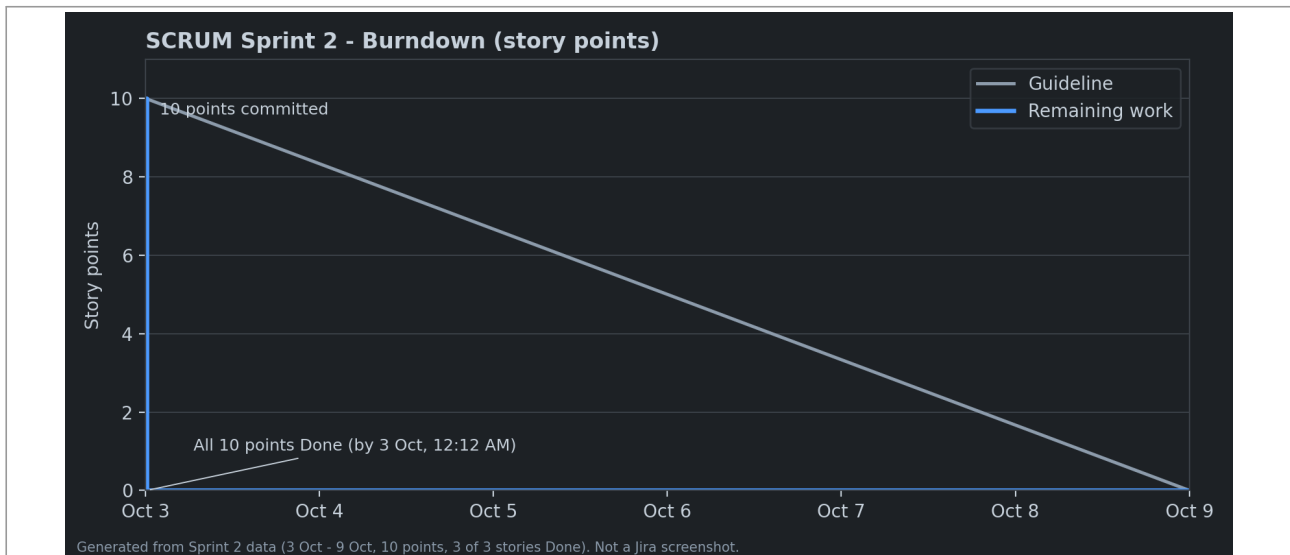

4. Reflection Questions

1. Did your estimations reflect the actual effort?

Partly. Because this was a simulated sprint, stories were closed within a short time, so the points cannot be compared with real hours. Judged by relative complexity, the sizing was reasonable. Check Book Availability (5) is the largest story because it depends on both the catalog data and the current loan and hold status of each copy. Add a Book to Catalog, Search Books by ISBN and Update Book Information (3 each) are standard create, read and edit work with validation, while View Book Details and Delete a Book from Catalog (2 each) are small changes on top of existing records. The weakness is that three stories share a 3, so the scale did not separate them much. With a real team, Planning Poker would have exposed differences in how each member sees the difficulty.

2. Was your backlog well-prioritized?

Yes. Add a Book to Catalog, Search Books by ISBN and Check Book Availability are High priority because members cannot find or reserve anything until the catalog holds books and can be searched. View Book Details and Update Book Information are Medium because they improve usability and accuracy but are not needed for the first working flow. Delete a Book from Catalog is Low because it is only needed for withdrawn titles. The stories were also scheduled in a logical order, with creation, search and viewing in Sprint 1, and maintenance, deletion and availability checking in Sprint 2. The epic itself was not given a separate priority, so priority was set at story level only.

3. How did your simulated sprint align with your plan?

Both sprints matched the plan. In Sprint 1, 8 points across 3 stories were committed and all three were moved to Done, meeting the sprint goal. In Sprint 2, the remaining 10 points across 3 stories were committed and completed. All 18 points (6 stories, 1 epic) were delivered. The main lesson is that stories should be estimated and prioritised before a sprint is started, so that the sprint insights and burndown begin from the correct commitment.

4. What insights did the burndown chart give about your team's capacity?

Both burndown charts drop steeply from the committed points to zero (8 to 0 in Sprint 1 and 10 to 0 in Sprint 2) instead of following the diagonal guideline. This is because the work was simulated and stories were moved to Done in one sitting, so the charts show no gradual progress and cannot reveal real capacity. In a real project, a drop like this would suggest that work was not tracked incrementally or that stories were not broken down well enough. What the data does show is that 100% of the committed points were delivered in both sprints, an average of 9 points per sprint (8 in Sprint 1 and 10 in Sprint 2). To measure true velocity, story status would need to be updated daily across the full sprint.
